


C:\Users\Renee_Culmer\Dropbox (AID)\1-PROJECTS (1)\BKV\BKV20017 - Runway 9-27 Extension\03-Drawings\EXHIBITS\RW 9-27 TENANT INFO.dwg Tab: 22 X 34 Feb 21, 2022 - 5:10pm Plotted by: Renee Culmer

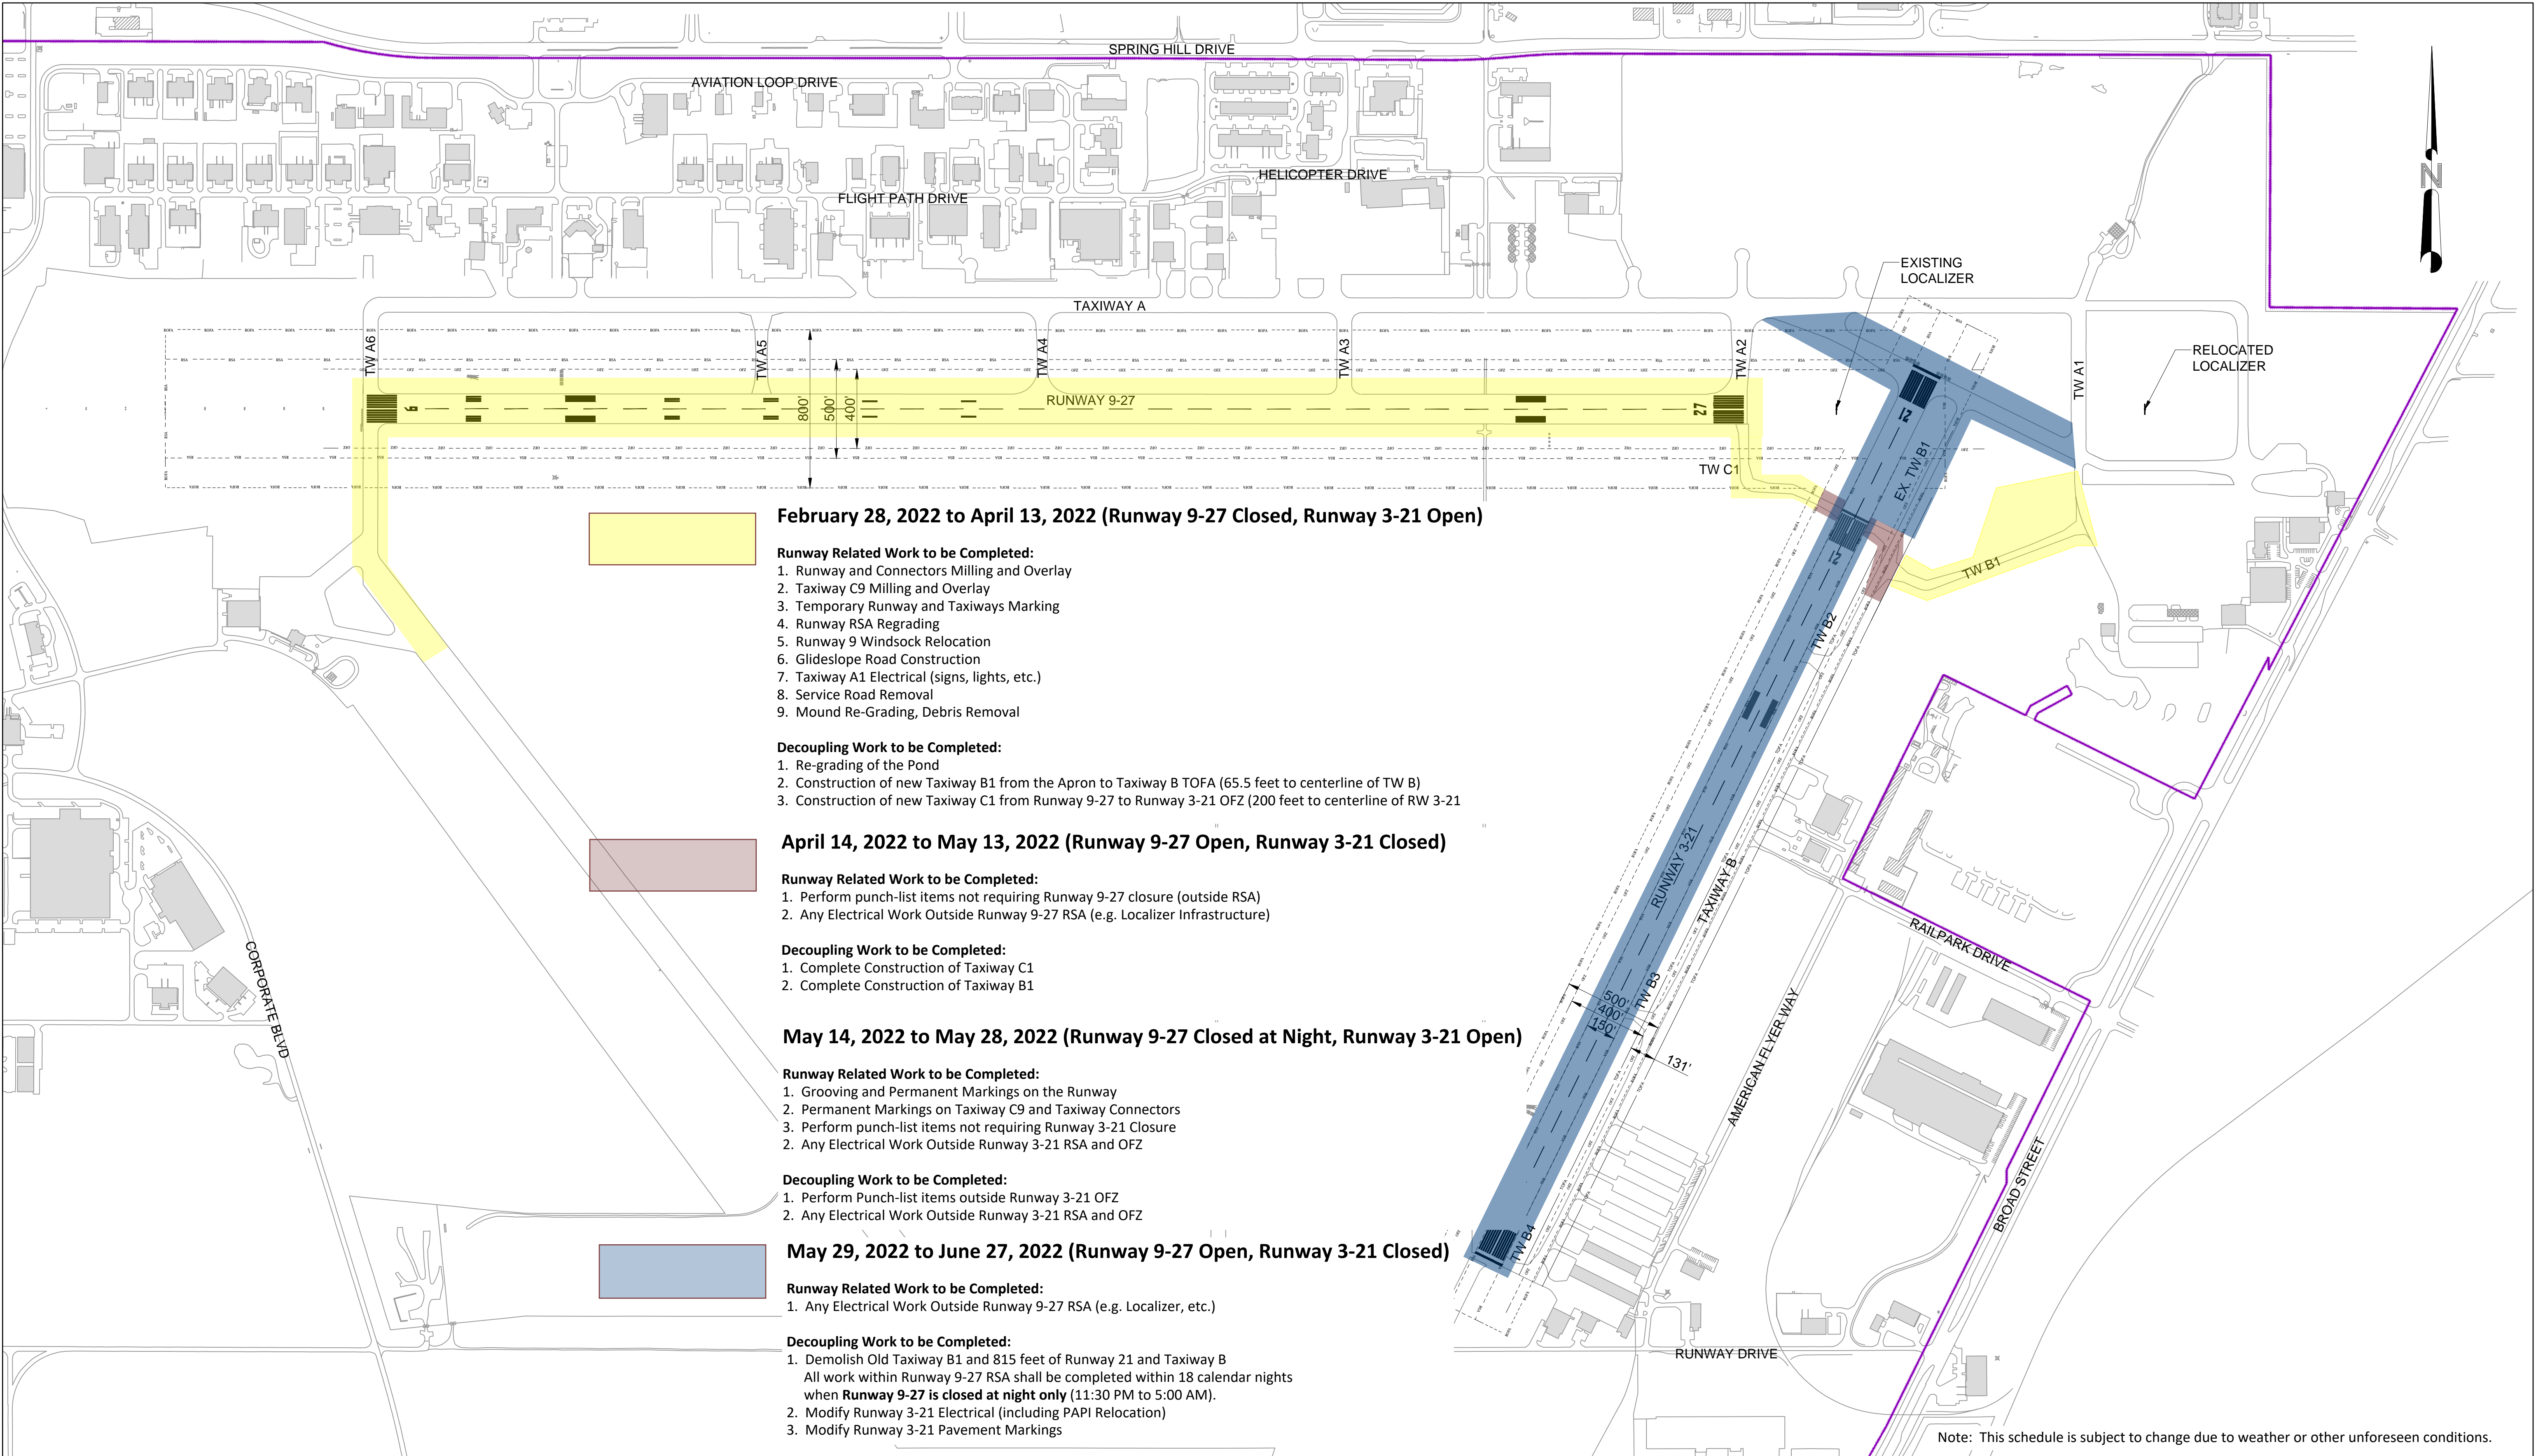

February 28, 2022 to April 13, 2022 (Runway 9-27 Closed, Runway 3-21 Open)

Runway Related Work to be Completed:

1. Runway and Connectors Milling and Overlay
2. Taxiway C9 Milling and Overlay
3. Temporary Runway and Taxiways Marking
4. Runway RSA Regrading
5. Runway 9 Windsock Relocation
6. Glideslope Road Construction
7. Taxiway A1 Electrical (signs, lights, etc.)
8. Service Road Removal
9. Mound Re-Grading, Debris Removal

Decoupling Work to be Completed:

1. Re-grading of the Pond
2. Construction of new Taxiway B1 from the Apron to Taxiway B TOFA (65.5 feet to centerline of TW B)
3. Construction of new Taxiway C1 from Runway 9-27 to Runway 3-21 OFZ (200 feet to centerline of RW 3-21)

April 14, 2022 to May 13, 2022 (Runway 9-27 Open, Runway 3-21 Closed)

Runway Related Work to be Completed:

1. Perform punch-list items not requiring Runway 9-27 closure (outside RSA)
2. Any Electrical Work Outside Runway 9-27 RSA (e.g. Localizer Infrastructure)

Decoupling Work to be Completed:

1. Complete Construction of Taxiway C1
2. Complete Construction of Taxiway B1

May 14, 2022 to May 28, 2022 (Runway 9-27 Closed at Night, Runway 3-21 Open)

Runway Related Work to be Completed:

1. Grooving and Permanent Markings on the Runway
2. Permanent Markings on Taxiway C9 and Taxiway Connectors
3. Perform punch-list items not requiring Runway 3-21 Closure
2. Any Electrical Work Outside Runway 3-21 RSA and OFZ

Decoupling Work to be Completed:

1. Perform Punch-list items outside Runway 3-21 OFZ
2. Any Electrical Work Outside Runway 3-21 RSA and OFZ

May 29, 2022 to June 27, 2022 (Runway 9-27 Open, Runway 3-21 Closed)

Runway Related Work to be Completed:

1. Any Electrical Work Outside Runway 9-27 RSA (e.g. Localizer, etc.)

Decoupling Work to be Completed:

1. Demolish Old Taxiway B1 and 815 feet of Runway 21 and Taxiway B
All work within Runway 9-27 RSA shall be completed within 18 calendar nights when Runway 9-27 is closed at night only (11:30 PM to 5:00 AM).
2. Modify Runway 3-21 Electrical (including PAPI Relocation)
3. Modify Runway 3-21 Pavement Markings

Note: This schedule is subject to change due to weather or other unforeseen conditions.

REV.	DATE	REVISIONS: DESCRIPTION:	BY



BROOKSVILLE-TAMPA BAY REGIONAL AIRPORT RUNWAY 9-27 REHABILITATION AND RUNWAYS DECOUPLING PHASING PLAN

DATE: FEBRUARY 21, 2022
